SHIVANSH / ONGC BRRP — OVERALL PROJECT SCHEDULE P5

PROPOSED SCENARIO | assumed NOA 1 Nov 2026 |12 months contractual basis | durations/resources unverified

Red: phase with critical child work. Blue: other work. Shaded:16 May–15 Oct offshore closure. Bars show last workdays.

PHASE / PACKAGE	START — LAST WORKDAY
G010 | COMMON | Kick-off, obligations, guarantees	2026-11-01 — 2026-11-07
E010 | COMMON | Design basis and interface approv	2026-11-08 — 2026-11-21
G020 | COMMON | Controlled document / addendum an	2026-11-08 — 2026-11-21
MR10 | COMMON | Vessel market enquiry, technical	2026-11-08 — 2026-12-12
S010 | COMMON | Survey permits, mobilisation and	2026-11-08 — 2026-11-14
S020 | ALL | Bridge and platform verification	2026-11-15 — 2026-11-28
E020 | ALL | Checked material requisitions / e	2026-11-29 — 2026-12-08
E030 | REPLACEMENTS | Detailed design, AFC drawings and	2026-11-29 — 2026-12-23
E040 | REFURBISHMENTS | Bridge and jacket strengthening d	2026-11-29 — 2026-12-23
E050 | BHS-SLQ | Utility transfer, temporary stabi	2026-11-29 — 2027-01-02
MR20 | REPLACEMENTS | Lift, loadout, transport and sea-	2026-12-24 — 2027-01-27
P010 | ALL | Vendor approval, steel purchase a	2026-12-09 — 2027-01-02
F010 | ICW-ICG LD | Fabricate, NDT, dimensional inspe	2027-01-03 — 2027-02-06
F020 | BHS-SLQ | Fabricate, NDT, dimensional inspe	2027-01-03 — 2027-02-26
F030 | ICG-ICP LD | Fabricate, NDT, dimensional inspe	2027-02-07 — 2027-03-18
F040 | ALL STRENGTHENING | All strengthening kits available	2027-01-03 — 2027-02-06
L010 | ICW-ICG LD | Loadout, sea-fastening and transp	2027-02-07 — 2027-02-11
L020 | BHS-SLQ | Loadout, sea-fastening and transp	2027-02-27 — 2027-03-03
L030 | ICG-ICP LD | Loadout, sea-fastening and transp	2027-03-19 — 2027-03-23
O010 | ALL | Accommodation/support mobilisatio	2027-01-23 — 2027-02-01
H010 | COMMON | Heavy-lift spread mobilisation an	2027-02-02 — 2027-02-08
J010 | ICG / BHS | Addendum jacket strengthening and	2027-02-02 — 2027-02-13
I010 | ICW-ICG LD | Install, connect, inspect and acc	2027-02-14 — 2027-03-01
I020 | BHS-SLQ | Install new bridge, transfer serv	2027-03-04 — 2027-03-23
D020 | BHS-SLQ | Isolate, dismantle old bridge and	2027-03-24 — 2027-03-30
J020 | ICP | Addendum jacket strengthening and	2027-02-02 — 2027-02-11
I030 | ICG-ICP LD | Install, connect, inspect and acc	2027-03-31 — 2027-04-17
RA01 | ICW-ICG UD | Strengthening, inspection and bri	2027-02-14 — 2027-03-01
RA02 | ICG-ICP UD | Strengthening, inspection and bri	2027-03-02 — 2027-03-23
RA03 | SLQ-WIS | Strengthening, inspection and bri	2027-03-24 — 2027-04-10
RA04 | NQO-NQD | Strengthening, inspection and bri	2027-02-07 — 2027-02-24
RB01 | WIN-NC | Strengthening, inspection and bri	2027-02-12 — 2027-02-23
RB02 | SCA-SC1 | Strengthening, inspection and bri	2027-02-24 — 2027-03-11
RB03 | SCA-SCF | Strengthening, inspection and bri	2027-03-12 — 2027-04-04
D030 | OTHER BRIDGES | Other removal, waste backload and	2027-04-18 — 2027-04-24
O090 | ALL | Final offshore inspections, punch	2027-04-25 — 2027-05-01
C010 | ALL | As-built dossiers, e-MB records,	2027-05-02 — 2027-05-31
W010 | ALL | Offshore weather / access allowan	2027-05-02 — 2027-05-11
O100 | ALL | Offshore demobilisation	2027-05-12 — 2027-05-14
C020 | ALL | Final document review and complet	2027-06-01 — 2027-06-14

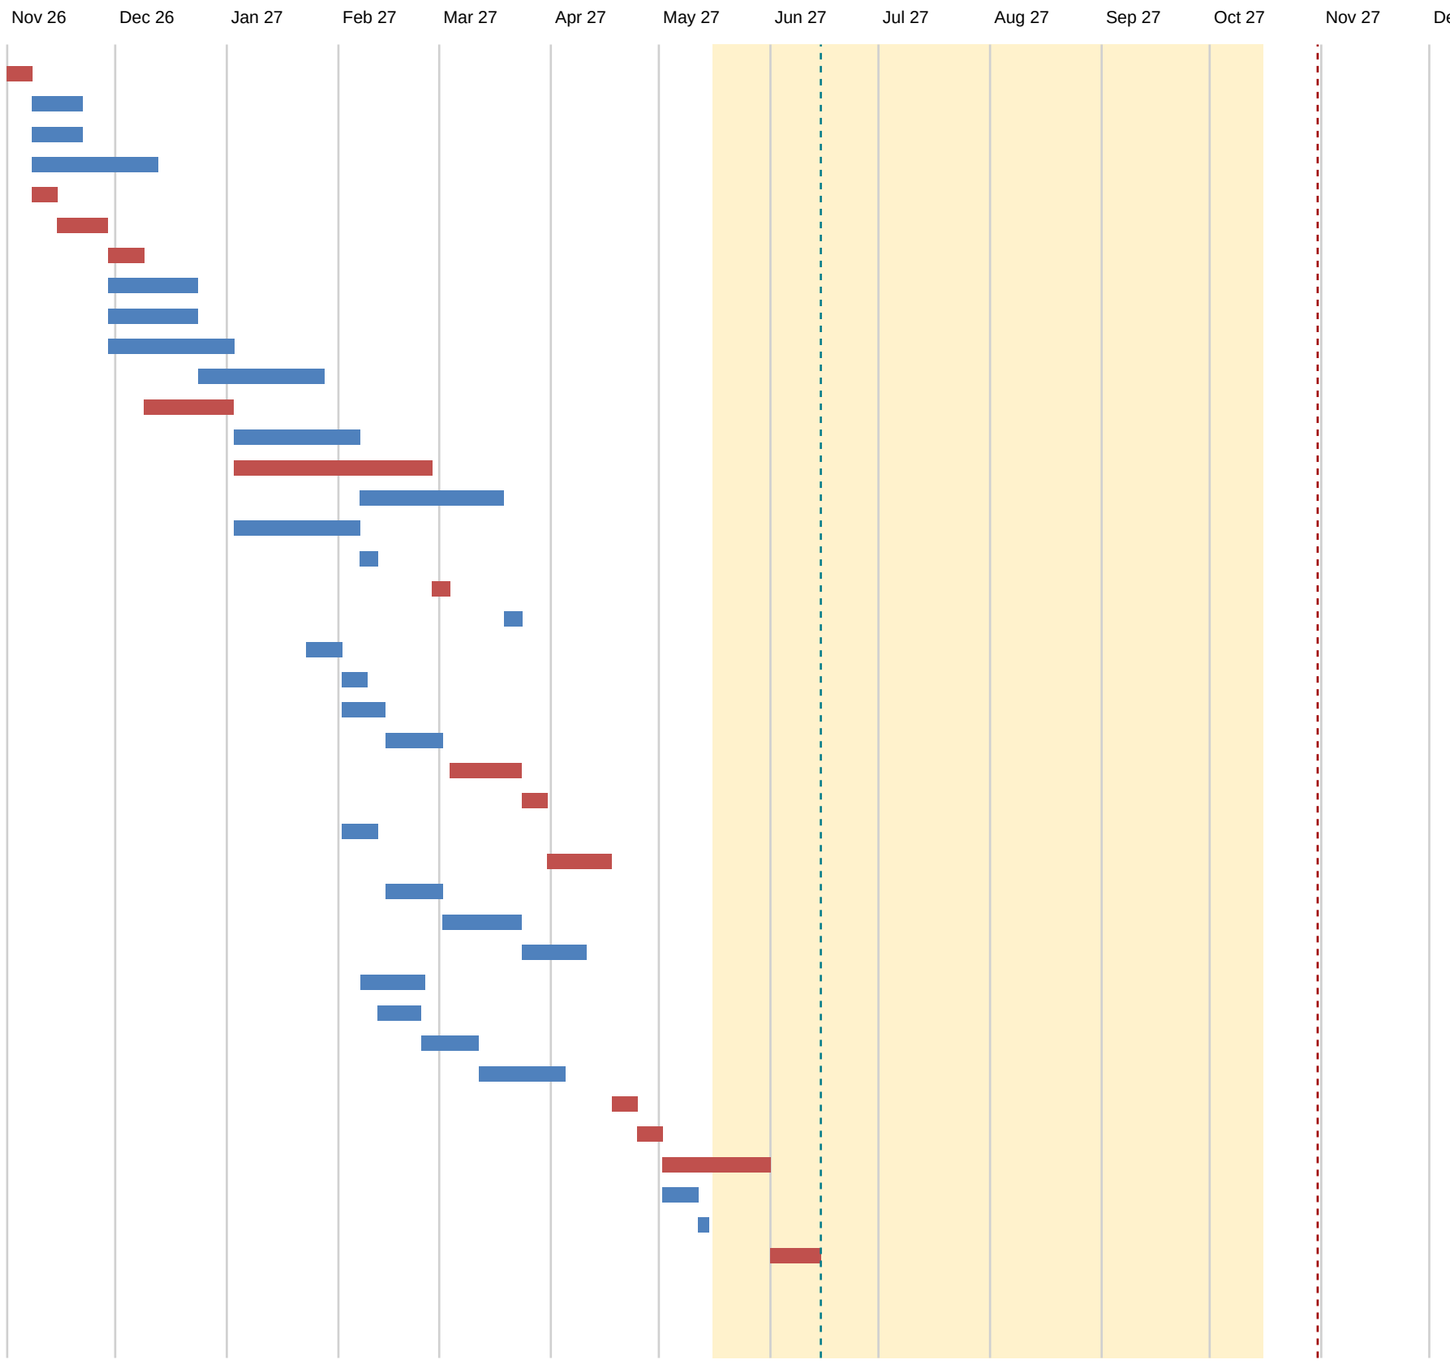

Critical route: materials → BHS fabrication/installation/services → BHS demolition → ICP installation → offshore closure → dossiers/acceptance.

Calendar sensitivity is significant. Validate actual NOA, workability, safe seasonal suspension, procurement lead times and all resource commitments.
