BRRP P14 — Calendar-aware schedule scenario

Not an approved forecast. Assumed start 1Nov 2026. Base completion 6Apr 2028. Target feasibility remains unresolved. Finish dates are exclusive boundaries.

Bridge	AFCgate	Ready loadout	Offshore punch end	Dossier end
ICW-ICG UD	2027-03-17	2027-10-30	2027-12-19	2028-01-01
ICW-ICG LD	2027-04-03	2027-09-14	2027-12-14	2027-12-28
ICG-ICP UD	2027-03-17	2027-11-21	2028-01-06	2028-01-20
ICG-ICP LD	2027-04-03	2027-10-19	2027-12-16	2027-12-30
BHS-SLQ	2027-04-03	2027-09-02	2027-12-12	2027-12-25
SLQ-WIS	2027-03-17	2027-12-03	2028-01-12	2028-01-26
NQO-NQD	2027-03-17	2027-12-19	2028-01-28	2028-02-11
WIN-NC	2027-03-17	2027-12-31	2028-02-02	2028-02-16
SCA-SC1	2027-03-17	2028-01-12	2028-02-13	2028-02-26
SCA-SCF	2027-03-17	2028-01-23	2028-03-09	2028-03-23

Driving path: survey → BHSdesign/review → steel → fabrication queue → coating queue → final strengthening/services/removal → dossiers → acceptance. Shared capacity and approval dependencies are explicit; actual productivity and bookings are unverified.

Alternative scenarios: 4 bays×8 MT/day finish 26Feb 2028; reducing steel supply 45→15 calendar days gives no further completion improvement under the same other assumptions. Neither is a contractual recovery promise.

Bridge-level timeline — scenario

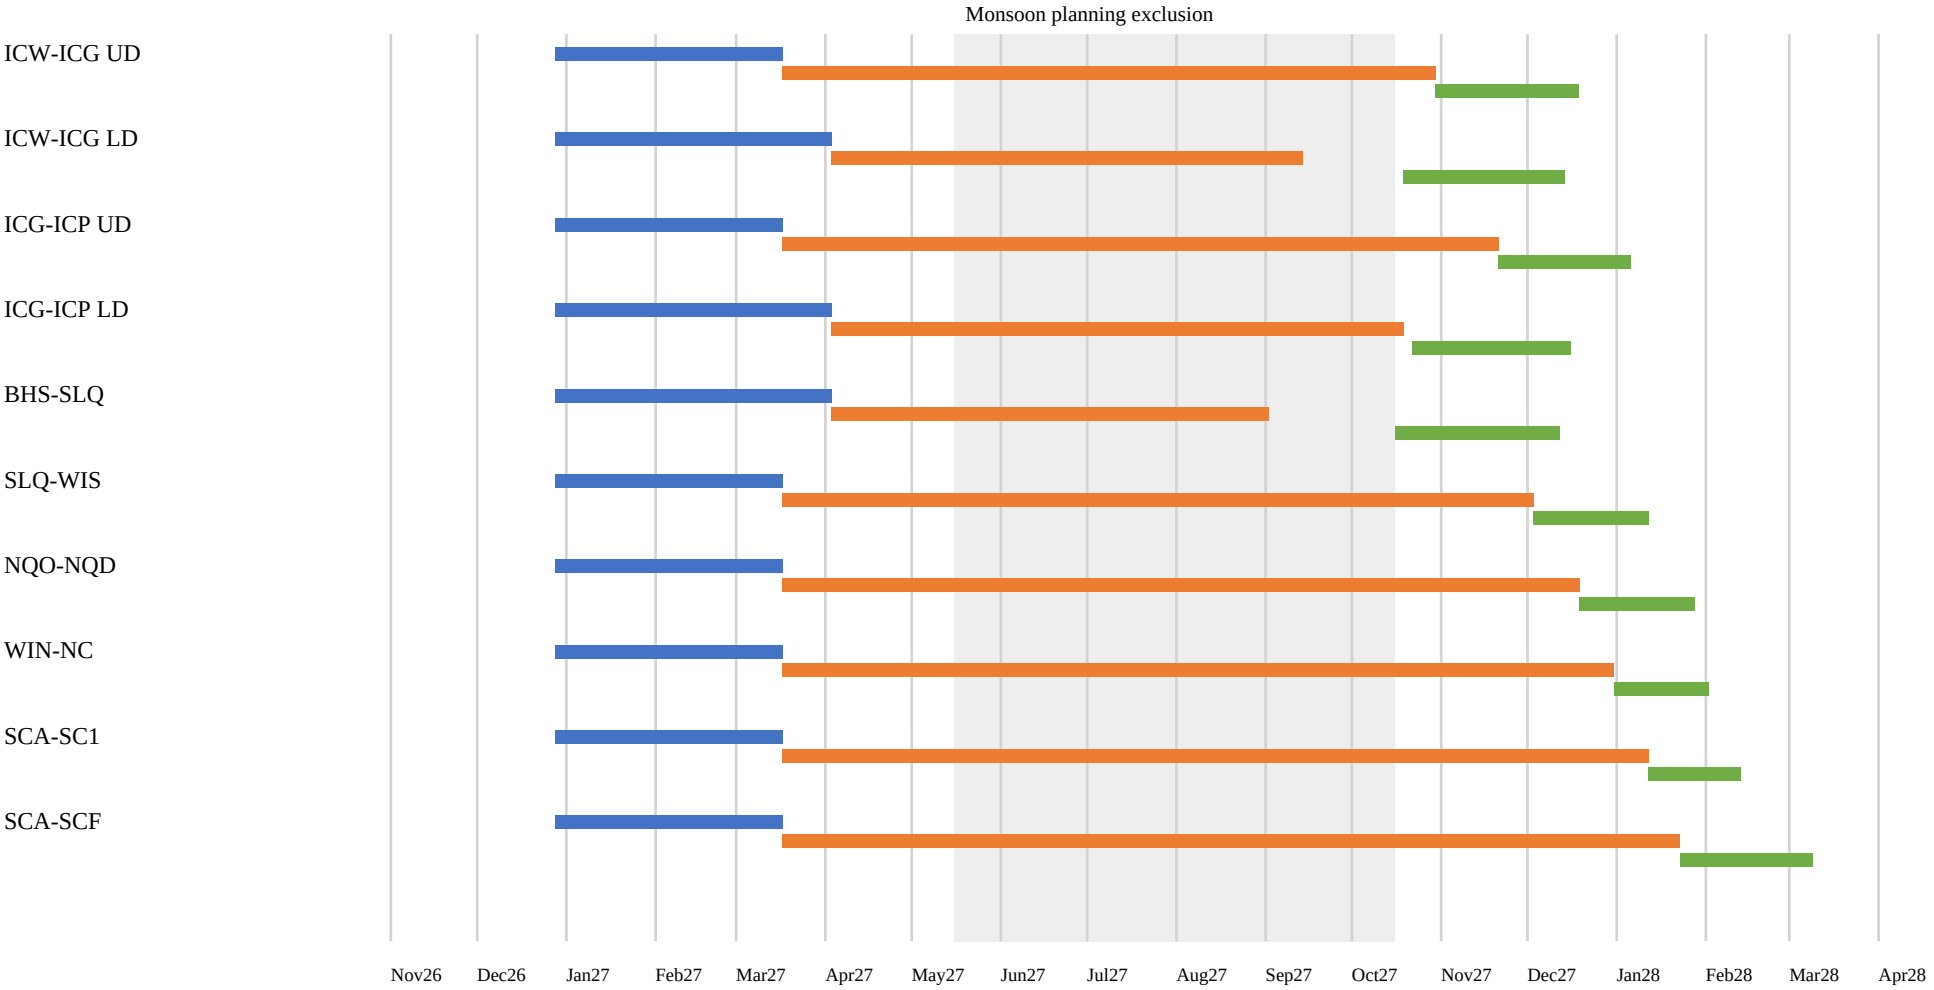

Blue engineering | Orange material/fabrication | Green offshore span (may include waiting)

Driving-chain activities

ID	Activity	Start	Finish exclusive
START	Assumed commencement — scenario only	2026-11-01	2026-11-01
G01	Contract/amendment matrix and scope reconciliation	2026-11-02	2026-11-07
G02	Survey permits, access and mobilisation preparation	2026-11-09	2026-11-21
G03	Pre-engineering survey campaign	2026-11-21	2026-12-06
G04	Survey reports, geometry/condition reconciliation	2026-12-07	2026-12-12
G05	Survey/basis review and comment closure allowance	2026-12-14	2026-12-26
B05-BAS	Design basis, loads and interfaces	2026-12-28	2027-01-02
B05-BRV	Basis review and comment closure allowance	2027-01-04	2027-01-16
B05-ANA	Bridge/platform and preservice analysis preparation	2027-01-18	2027-02-13
B05-ARV	Analysis review and comment closure allowance	2027-02-15	2027-02-27
B05-DET	Connection, bearing, landing and workpack detailing	2027-03-01	2027-03-20
B05-DRV	Drawing review and comment closure allowance	2027-03-22	2027-04-03
B05-AFC	AFC design/MTO independent check and release gate	2027-04-03	2027-04-03
B05-PO	Bridge steel compliant PO release gate	2027-04-03	2027-04-03
B05-MAT	Mill production, inspection and steel delivery	2027-04-03	2027-05-18
B05-FAB	Fit-up, welding and dimensional control	2027-05-18	2027-08-08
B04-FAB	Fit-up, welding and dimensional control	2027-08-09	2027-09-24
B03-FAB	Fit-up, welding and dimensional control	2027-09-24	2027-10-28
B07-FAB	Fit-up, welding and dimensional control	2027-10-28	2027-11-25
B07-NDT	NDT, repair allowance and dimensional release	2027-11-25	2027-12-02
B07-COA	Surface preparation, coating and curing allowance	2027-12-02	2027-12-14
B08-COA	Surface preparation, coating and curing allowance	2027-12-14	2027-12-25
B09-COA	Surface preparation, coating and curing allowance	2027-12-25	2028-01-06
B10-COA	Surface preparation, coating and curing allowance	2028-01-06	2028-01-18
B10-REL	Trial fit, verified weight/COG and loadout release	2028-01-18	2028-01-23
B10-TRN	Loadout, transport and offshore receipt	2028-01-23	2028-01-26

ID	Activity	Start	Finish exclusive
B10-PRE	PTW, access, SIMOPS and work-front readiness	2028-01-26	2028-01-29
B10-STR	Landing/platform pre-install strengthening	2028-01-29	2028-02-05
B10-INS	Bridge strengthening and replacement items	2028-02-05	2028-02-28
B10-SRV	Services transfer, test and accepted reinstatement	2028-02-28	2028-03-04
B10-DEM	Engineered demolition/removal and scrap backload	2028-03-04	2028-03-06
B10-PUN	Inspection, touch-up and offshore punch closure	2028-03-06	2028-03-09
B10-DOS	As-built, QA and turnover dossier acceptance	2028-03-09	2028-03-23
CLOSE	Integrated acceptance, final measurements and account preparation	2028-03-23	2028-04-06
FINISH	Proposed contract-completion milestone	2028-04-06	2028-04-06
